Exhibit "B"

PRESCOTT VALLEY

Town of Prescott Valley
7501 E. Civic Circle
Prescott Valley, AZ 86314

July 25, 2011

Catherine Korte
Fann Contracting, Inc.
P.O. Box 4356
Prescott, Arizona 86302

Project: Robert Road Improvements – Spouse to Tranquil - CIP # 412B
Re: Extension of Contract Time

Dear Ms. Korte,

The contract time for the above referenced project is 180 calendar days. Per your written request, and upon recommendation of the project engineer, Kirkham Michael, the contract time is hereby extended 24 calendar days per M.A.G. specifications.

The new project completion date is September 28, 2011.

Please submit a revised schedule for the construction of this project.

We appreciate your work in making this project a success. If you have any questions, do not hesitate to contact me or the Project Manager, Ray Smith, at (928) 759-3075.

Sincerely,

Ron Pine, P.E., Engineer
(928) 759-3035
Email: rpine@pvaz.net

Enclosures: Recommendation Letter from Kirkham Michael dated July 25, 2011
Time Extension Request from Fann Contracting dated July 7, 2011

cc: Steve Irons, P.E. - Construction Engineer
Ray Smith, P.E., R.L.S. - Project Manager
Norm Davis, P.E. - Public Works Director
Diane Russell - Town Clerk
File

KIRKHAM MICHAEL

Arizona • Colorado
Iowa • Kansas • Nebraska

www.kirkham.com

July 25, 2011

RE: Recommendation for Time Extension of 24 Calendar Days
Robert Road Improvements
KM-1012239

Town of Prescott Valley
Public Works Department
Attn: Ray Smith, P.E.
7501 E. Civic Circle
Prescott Valley, AZ 86314

Mr. Ray Smith,

Kirkham Michael has reviewed the "Time Extension Request Letter from Fann Contracting dated July 7, 2011" and MAG specifications section 105.6 and 108.7 to justify providing a contract adjustment to the time of completion for the project. Upon review of the provided project schedule and MAG specification section 105.6 and 108.7, we recommend that the project contract time of completion be extended by 24 calendar days. The additional 24 calendar days added to the project contract time of completion, in addition to already compensated costs provided for extra work shall constitute full compensation for the project time extension.

Please give me a call at 1.402.477.4240 if you have any questions.

Sincerely,

KIRKHAM MICHAEL

Steve Irons

Steve Irons
Project Manager

SI

Encl. Time Extension Request Letter

Copy to: File, Norm Davis, Ron Pine, Scott Lyon

411 South 13th, Suite 101 • P.O. Box 83328 • Lincoln, NE 68508 • (402) 477-4240 • FAX (402) 477-4268

FANN Contracting, Inc.
PO Box 4356 • Prescott, AZ 86302 • Phone 928.778.0170 • Fax 928.778.3072 • ROC-A-071520

July 7, 2011

Kirkham Michael and Associates, Inc.
PO Box 83328
Lincoln, NE 68501

Attn: Mr. Steve Irons
Project Engineer

Re: Robert Road Improvements-Spouse to Tranquil
Time Extension Request

Dear Mr. Irons:

In accordance our discussion at the weekly meeting of June 30th, we respectfully request a time extension change order be executed for the various delays and extra work performed on this project as documented in the schedule updates provided to you each week.

In accordance with the current schedule update (copy attached), we hereby request 24 days be added to the contract time to compensate for the delays experienced and extra work requested through the period ending June 30, 2011.

Thank you for your consideration in this matter. If you have any questions or need additional information, please do not hesitate to contact our office.

Sincerely,

Catherine Korte

Catherine Korte
Project Manager

Enclosure

cc: Mike Shivers, Scott Lyon, Ron Pine

Description	Early Start	Early Finish
Notice to Proceed	08MAR11	
Mobilization	08MAR11	10MAR11
Survey-Clearing Limits/Rdwy Exc	08MAR11	14MAR11
Clear and Grub/Misc. Removals	08MAR11	10MAR11
Traffic Control Set-Up	08MAR11	15MAR11
Asphalt Milling	14MAR11	15MAR11
SWPP Installation	16MAR11	22MAR11
Roadway Excavation	16MAR11	06APR11
*Weather Delay (2 days)	21MAR11	22MAR11
*Delay-Waterline Break (2 days)	28MAR11	29MAR11
Survey-Storm Drain	06APR11	07APR11
Storm Drain Installation	06APR11	26MAY11
Sewer Service Reconstructions	07APR11	27APR11
*Delay-Gas Line Conflict (1 day)	11APR11	11APR11
*Delay-Hit Unmarked Gas Line (1 day)	13APR11	13APR11
*Delays-Qwest Sewer/SD Conflicts (1 day)	25APR11	26APR11
*Delay-Exist Util/SD Conflicts Jacque (1/2 day)	27APR11	27APR11
*Delay-SD Conflict w/Gas-Harlequin (1/2 day)	02MAY11	02MAY11
*Delays-SD Conflicts-Manley,Tranquil (1 day)	09MAY11	10MAY11
Survey-Water	10MAY11	12MAY11
Sewer Service Extensions	11MAY11	12MAY11
*Extra work-Vertical Realignment (1 day)	16MAY11	17MAY11
Water Installation	16MAY11	13JUN11
*Delay-SD Conflict w/Gas-Judy Cir.(1/2 day)	19MAY11	19MAY11
*Delay-SD Conflict w/Gas-Sta 112+18 (2 days)	23MAY11	24MAY11
*Water Delay-Gas Co installing drop (2 days)	25MAY11	26MAY11
*Water Delay-Conflict w/Qwest (1 day)	02JUN11	02JUN11
Concrete Prep/ABC	06JUN11	29JUN11
Survey-ROW	07JUN11	08JUN11
*Extra Work-Water Line Changes (2 days)	09JUN11	13JUN11
*Delay-Gas Line/Subgrade-Tranquil (3 days)	13JUN11	15JUN11
Water Line Testing/Tie-ins	14JUN11	24JUN11
Concrete Curb and Gutter	14JUN11	07JUL11
*Delay-CableOne relocating lines (4 days)	20JUN11	23JUN11
Concrete Catch Basins	27JUN11	14JUL11
Install Street Light Conduits	27JUN11	14JUL11
Concrete Headwall	01JUL11	06JUL11
Subgrade Prep	07JUL11	13JUL11
Concrete Sidewalks/Scuppers/Driveways	08JUL11	25JUL11
Fencing	11JUL11	19JUL11
Survey-Subgrade Bluetops	12JUL11	13JUL11
Place/Finish ABC - Roadway	13JUL11	21JUL11
Survey-ABC Bluetops	21JUL11	22JUL11
AC Paving	25JUL11	28JUL11
Handrail	26JUL11	02AUG11
Temporary Striping	28JUL11	28JUL11
Permanent Relocation Signs/Mailboxes	28JUL11	08AUG11
Adjust Valves/Manholes/Monuments	28JUL11	10AUG11
Install Street Lights	01AUG11	04AUG11
Chip Seal	11AUG11	11AUG11
Temporary Striping	12AUG11	12AUG11
Substantial Completion	12AUG11	
Clean-up/Demobilization	15AUG11	18AUG11
Permanent Striping	13SEP11	14SEP11

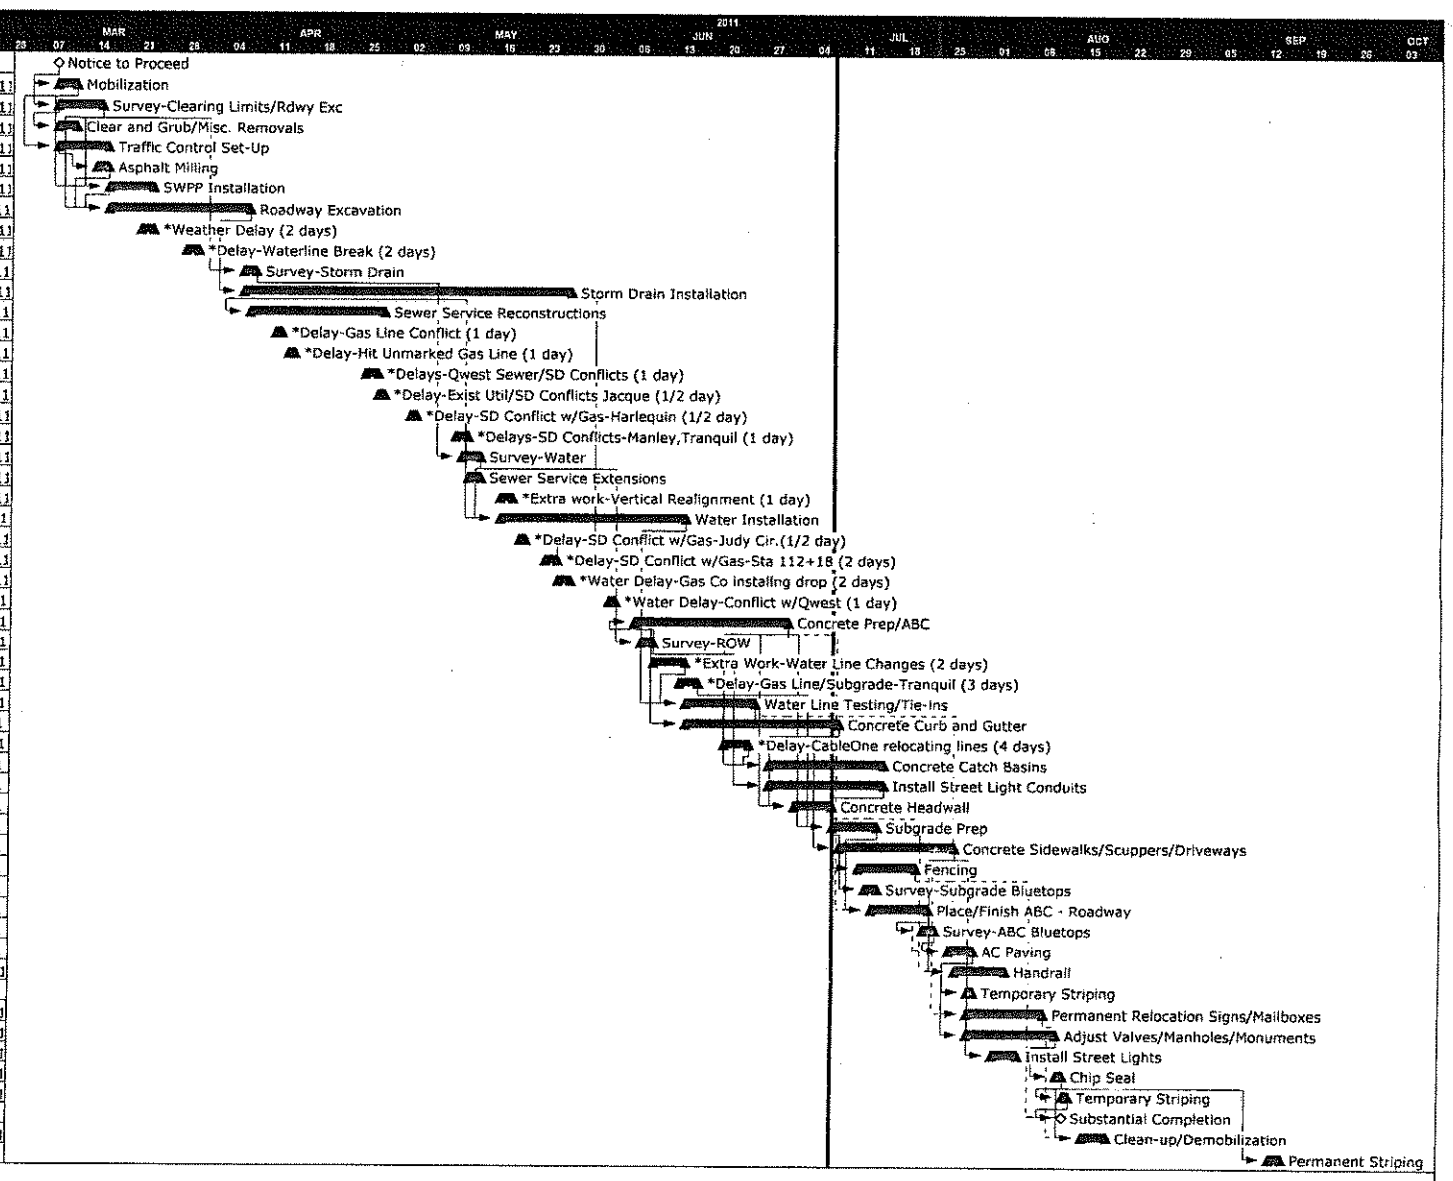

Start date	08MAR11
Finish date	14SEP11
Data date	07JUL11
Run date	06JUL11
Number/Version	11

© Primavera Systems, Inc.

Fann Contracting, Inc.
Robert Rd Improvements-Spouse to Tranquil
Construction Schedule Update

- Early bar
- Early start point
- Early finish point
- Critical point
- Start milestone point
- Finish milestone point
